






- Program Schedule
- FY 01 Installs
- Current Initiatives
- Training

SPAWAR V

NTCSS Program Schedule

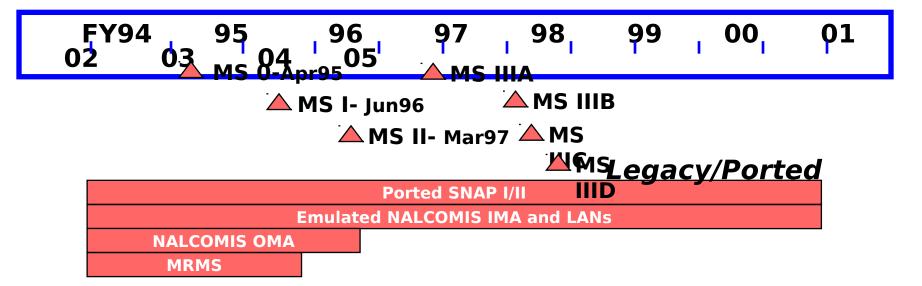

Optimized

R-Supply	Fielding/Deployment
OMMS-NG	Fielding/Deployment
R-ADMIN	Fielding/Deployment
NALCOMIS IMA	Fielding/Deployment

Hardware

Software Development



FY01 Installations (1st &

2nd Qtr)

Red denotes SSC Che	sapeake Install	Blue denotes SSC Che	s. Det San Diego	Install C denotes co	ompletion
<u>Jan 01</u>		<u>Feb 01</u>		<u>Mar 01</u>	
Site	Install	Site	Install	Site	Install
CG72 Vella Gulf	Full Optimize C	CVN 71 Teddy Roosevelt	Full Optimize	NAS Oceana	RSUP at NAS
CG55 Leyte Gulf	Full Optimize C	SSN 764 Boise	Full Optimize	NSCS Athens	Full Optimize
LSD 41 Whidbey Island Connecticut	Backfit Optimize Backfit Optimize	С	NAS Pensacola	Full Optimize	SSN 22 USS
FFG 55 Elrod	Full Optimize C Full Optimize	SSN 708 USS Minn. St Pa	ul	Backfit Optimize	LHD 7 IWO JIMA
FCTCLANT Dam Neck	Full Optimize C	DD985 Cushing	Backfit Optimize	SSN 762 Columbus	Full Optimize
LHA 5 Peleliu	Backfit Optimize Full Optimize	С	DDG 82 Lassen	Full Optimize	NAS Misawa
LSD 45 Comstock	Full Optimize C	CVN 68 Nimitz	NTCSS II	NATTC Pensacola	Full Optimize
LSD 42 Germantown	Full Optimize C	DDG 70 Hopper	Backfit Optimize	SSN 717 Salt Lake City	Full Optimize
SSN 759 Jefferson City	Full Optimize C	SSN 753 Albany	Full Optimize		
CG 54 Antietam	Full Optimize C				



FY01 Installations

Apr 01 ()		<u>May 01</u>		<u>Jun 01</u>	
Site	Install	Site	Install	Site	Install
SSN 700 USS Dallas Kennedy	Backfit Optimized Full Optimized	MALS 39	Backfit Optimized	d	CV 67 John F
NAF Atsugi Cook	Full Optimized Backfit Optimized	LHD 5 Bataan	Backfit Optimized	d	DDG 75 Donald
SSN 701 La Jolla Optimized	Full Optimized	NAS Meridian	Full Optimized	CG 73 Port Royal	Backfit
NAS Lemoore Optimized	RSUP at NAS	LSD 44 Gunston Hall	Full Optimized	LHD 6 BH Richard	Backfit
LHA 3 Belleau Wood Optimized	Backfit Optimized	CG 63 Cowpens	Full Optimized	DDG 73 Decatur	Backfit
SSN 707 Portsmouth	Full Optimized			SSN 720 Pittsburgh	Full Optimized
CG 59 Princeton	Backfit Optimized				
<u>Jul 01</u>			<u>Aug 01</u>		<u>Sep 01</u>
Site	Install	Site	Install	Site	Install
SSN 769 Toledo	Full Optimized	DDG84 Buckeley	Full Optimized	SSN 724 Louisville	Full Optimized
CG 49 Vincennes	Full Optimized	NAS Roosevelt Roads	Full Optimized	CG 62 Chancellorsville	Full Optimized

NAF Washington DC Full Optimized D Charles Was 1x z T Ten kh Charles mile H

Full Optimized

Full Optimized

Full Optimized

00/02/16

Full Optimized

Backfit Optimized CVN 68 Nimitz

Backfit Optimized SSN 773 Cheyenne

DDG 83 Howard

CV 63 Kitty Hawk

LSD 52 Pearl Harbor

SSN 766 Charlotte





- BCM
 - RSupply, OIMA complete
 - Awaiting TCT
 - Aspen Release
 - Feb 01
- RSupply Ashore
 - NAS Oceana
 - Birch Release
 - Apr 01
- Wizard Works ("In the Box")
 - IBS,FACTS,SMARTS,MAMS
- Serial Number Tracking
 - All applications affected
 - SNT in Aspen release
 - Cage/Part-Number/Serial-Number



Points of Contact

Code/Position	Name .	Phone Number	
PMW 151 Program Manager	CAPT Speer Ezzard	(619) 524-	
PMW 151A Deputy Program	Ms. Susan Linn	7553	
Manager		(619) 524-	
PMW 151-1	CDR Allen Booker	7555	
Customer Liaison Div.		(619) 524-	
PMW 151-2	Mr. Sam Anderson	7961	
System Acq. and Eng.		7501	
PMW 151-3	LCDR Mike Kelly	(619) 524-	
Requirements	Mr. Mike Crow	7564	
PD 15L Logistics Coordinator		(619) 524-	
DMW 151_4	Mr. Mike Taousakis	7669) 524-7545	

B្រុខ្លgram Development

http://c4iweb.spawar.navy.mil/pmw151/

(619) 524-7543

Training



- Install Training and Embedded Help
- School House Training (Inadequate)
 - OOMA/OIMA
 - Training Situational Analysis (TSA) and Job Task Analysis (JTA) completed
 - Navy Training Support Plan (NTSP) in draft.
 - AZ "C" school curriculum under development, due for pilot teach 11 Jun 01
 - Ready-For-Training in 4th Quarter FY01

Rsupply

- JTA completed
- NTSP under development
 - Rsupply curriculum development to begin 01 Mar 01
 - Ready-For-Training in FY01

R-Admin/OMMS-NG

- JTA Scheduled for mid Mar 01
 - Develop curriculum 4th Quarter FY01;
 - Ready-For-Training in FY02
- NTCSS Capstone NTSP under review by OPNAV.
